Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
George Green - Sitework Crew Foreman					
Carpenter					
P1N2200	12	16.00	192.00	27JUL99	11AUG99
Air Compressor & Hoses					
P1N2200	12	1.00	12.00	27JUL99	11AUG99
Truck Crane					
P1N1145	1	0.00	1.00	04NOV98	25NOV98
P1N1180	1	0.00	1.00	23DEC98	11JAN99
P1N1200	4	0.00	1.00	17FEB99	17MAR99
P1N1235	1	0.00	1.00	13MAY99	13MAY99
P1N2100	12	1.00	12.00	07JUN99	22JUN99
P1N2195	3	1.00	3.00	17JUN99	21JUN99
P2N3100	6	1.00	6.00	03SEP99	10SEP99
P2N3225A	5	1.00	5.00	13SEP99	17SEP99
P2N2198	4	1.00	4.00	31JAN00	03FEB00
Dozer, 200 H.P.					
P1G105	4	0.00	4.00	01OCT98	02OCT98
P1N1202	20	0.00	20.00	17DEC98	15JAN99
P1N1210	10	0.00	10.00	18MAR99	30MAR99
P1N2115A	8	1.00	8.00	23JUN99	02JUL99
P2N3120	7	1.00	7.00	24SEP99	04OCT99
P1N2240	9	1.00	9.00	27OCT99	08NOV99
P1N2250	7	1.00	7.00	09NOV99	17NOV99
Truck Driver - Heavy					
P1N2190	8	8.00	64.00	07JUN99	16JUN99
P1N2115A	8	24.00	192.00	23JUN99	02JUL99
P2N2196	9	8.00	72.00	18JAN00	28JAN00
Foreman					
P1G105	4	0.00	8.00	01OCT98	02OCT98
P1N1140	1	0.00	2.00	03NOV98	03NOV98
P1N1145	1	0.00	2.00	04NOV98	25NOV98
P1N1150	5	0.00	10.00	30NOV98	07DEC98

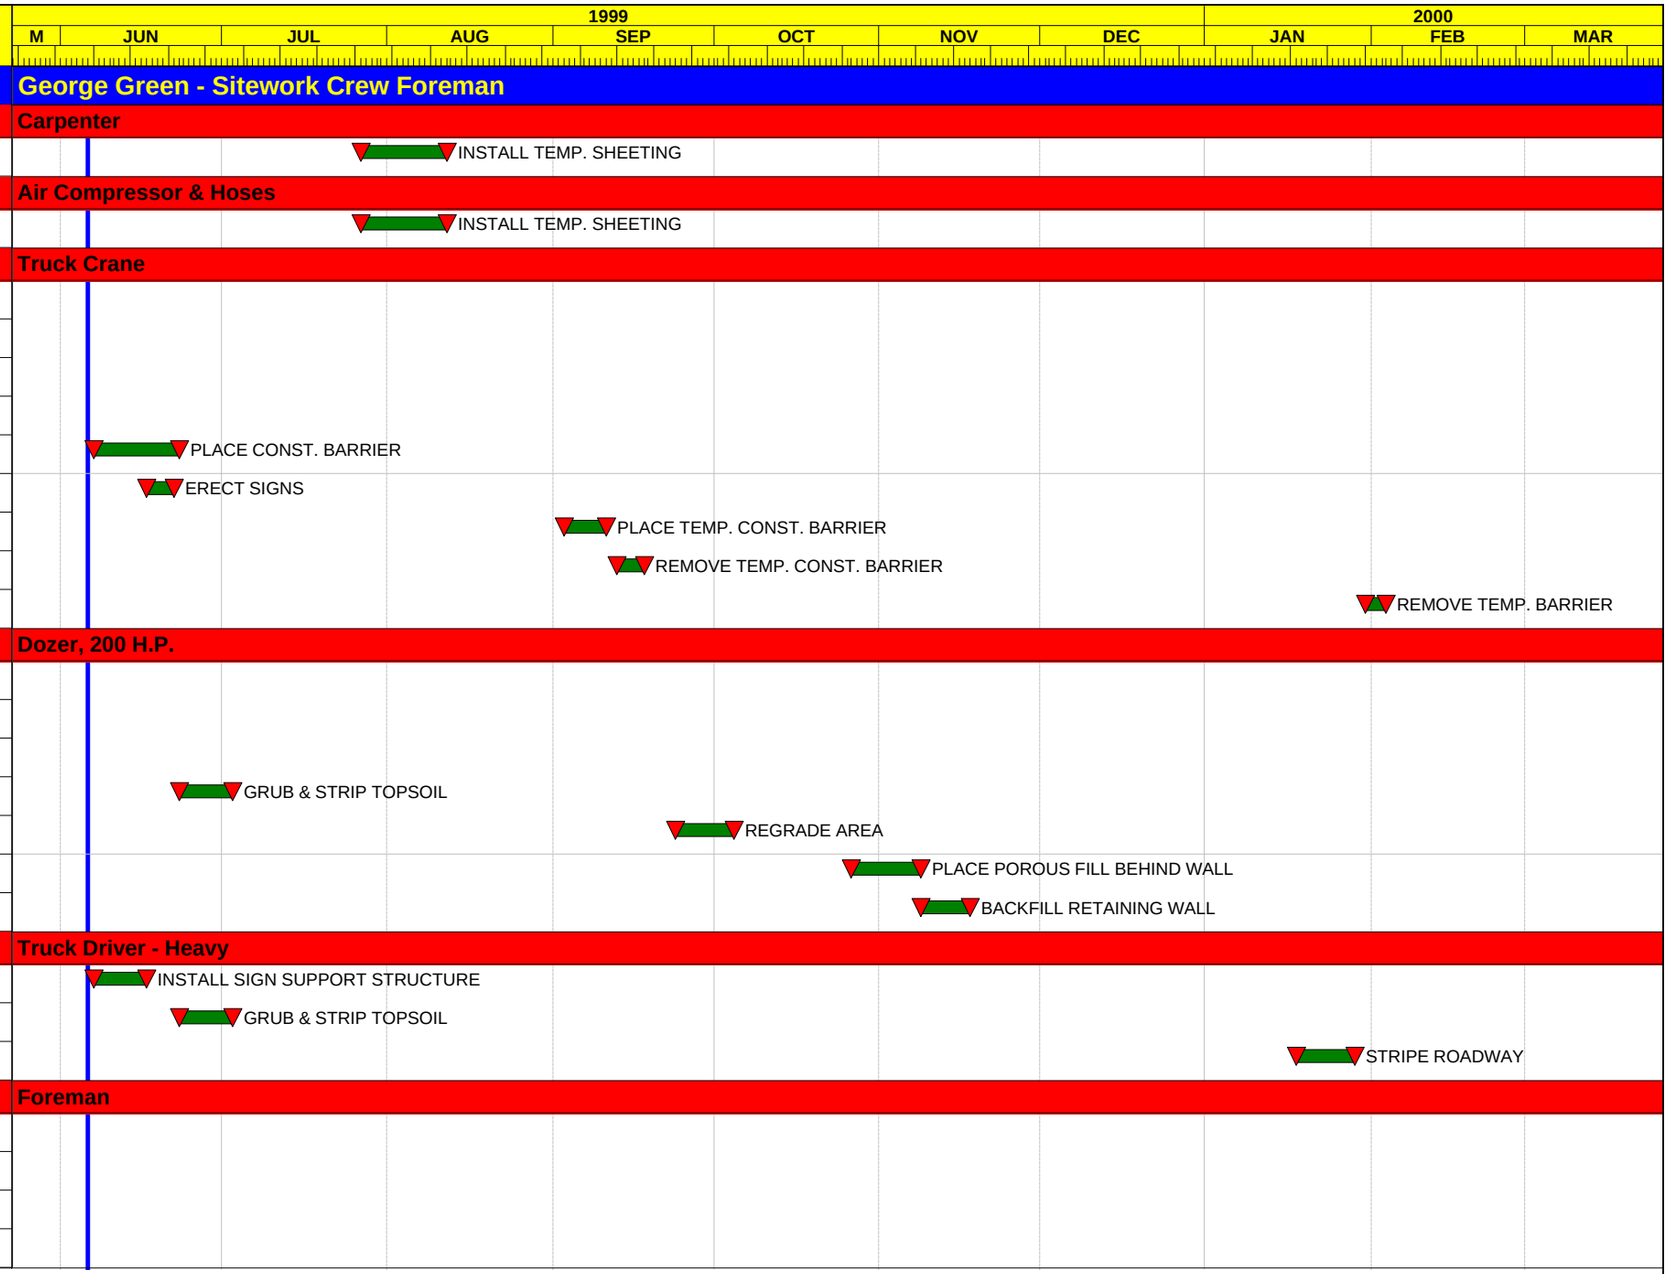

Project Start	24SEP98
Project Finish	28MAR00
Data Date	06JUN99
Run Date	25MAR99

Resource Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

HWY1

C.M. Construction, Inc.

Highway Widening

Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
P1N1202	20	0.00	40.00	17DEC98	15JAN99
P1N1180	1	0.00	2.00	23DEC98	11JAN99
P1N1195	1	0.00	2.00	01FEB99	09FEB99
P1N1200	4	0.00	2.00	17FEB99	17MAR99
P1N1210	10	0.00	20.00	18MAR99	30MAR99
P1N1235	1	0.00	2.00	13MAY99	13MAY99
P1N2100	12	2.00	24.00	07JUN99	22JUN99
P1N2190	8	2.00	16.00	07JUN99	16JUN99
P1N2195	3	2.00	6.00	17JUN99	21JUN99
P1N2115A	8	4.00	32.00	23JUN99	02JUL99
P1N2105B	15	0.13	2.00	06JUL99	26JUL99
P1N2200	12	2.00	24.00	27JUL99	11AUG99
P1N2210	12	2.00	24.00	12AUG99	27AUG99
P2N2115B	4	2.00	8.00	30AUG99	02SEP99
P2N2125A	10	2.00	20.00	03SEP99	16SEP99
P2N3100	6	2.00	12.00	03SEP99	10SEP99
P2N3110	9	2.00	18.00	13SEP99	23SEP99
P2N3225A	5	2.00	10.00	13SEP99	17SEP99
P2N3120	7	2.00	14.00	24SEP99	04OCT99
P1N2240	9	2.00	18.00	27OCT99	08NOV99
P1N2250	7	2.00	14.00	09NOV99	17NOV99
P2N2196	9	2.00	18.00	18JAN00	28JAN00
P2N2198	4	2.00	8.00	31JAN00	03FEB00
General Laborer					
P1G105	4	0.00	24.00	01OCT98	02OCT98
P1N1140	1	0.00	16.00	03NOV98	03NOV98
P1N1145	1	0.00	16.00	04NOV98	25NOV98
P1N1150	5	0.00	80.00	30NOV98	07DEC98
P1N1180	1	0.00	16.00	23DEC98	11JAN99
P1N1190	1	0.00	16.00	20JAN99	28JAN99
P1N1195	1	0.00	16.00	01FEB99	09FEB99

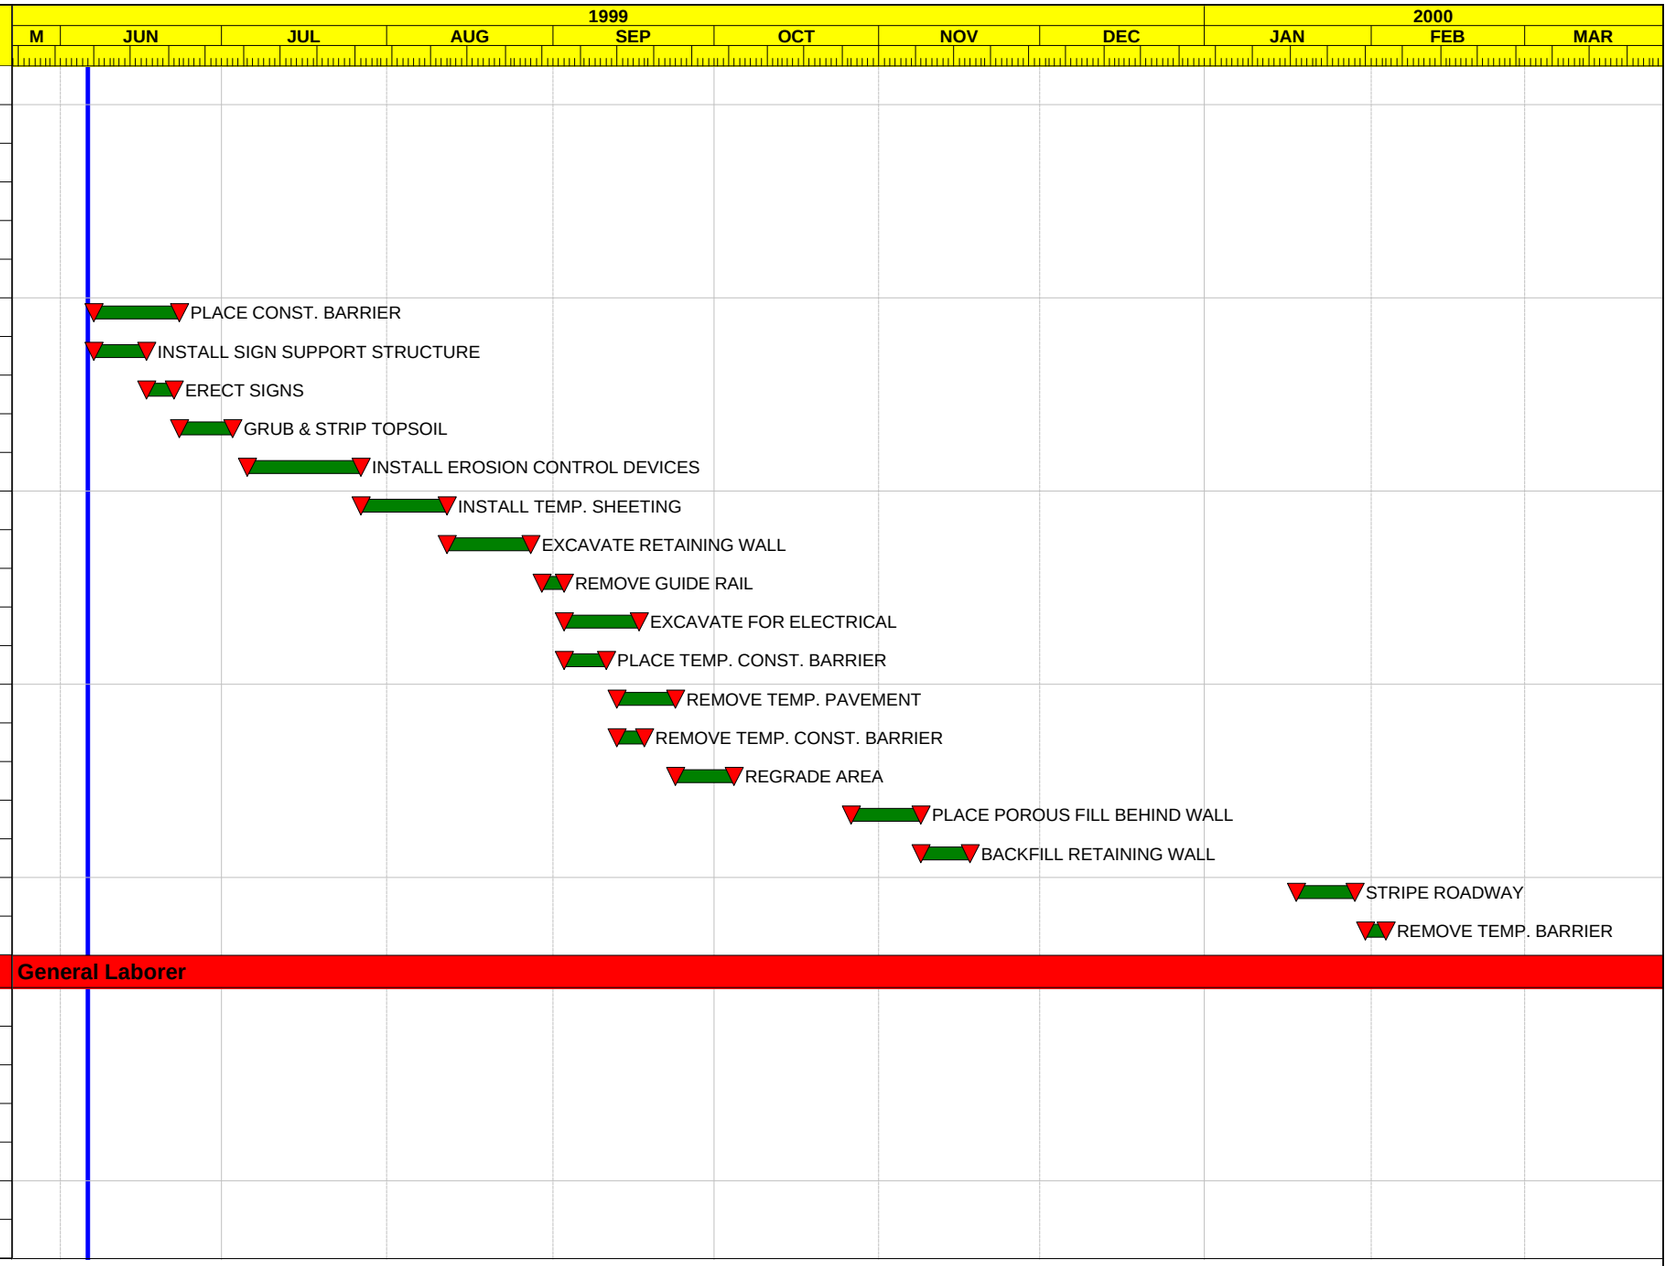

Project Start 24SEP98
Project Finish 28MAR00
Data Date 06JUN99
Run Date 25MAR99

Resource Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

HWY1

C.M. Construction, Inc.

Highway Widening

Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
P1N1200	4	0.00	32.00	17FEB99	17MAR99
P1N1235	1	0.00	8.00	13MAY99	13MAY99
P1N1240	1	0.00	16.00	20MAY99	02JUN99
P1N2100	12	8.00	96.00	07JUN99	22JUN99
P1N2190	8	8.00	64.00	07JUN99	16JUN99
P1N2195	3	16.00	48.00	17JUN99	21JUN99
P1N2105B	15	16.00	240.00	06JUL99	26JUL99
P1N2200	12	24.00	288.00	27JUL99	11AUG99
P1N2210	12	8.00	96.00	12AUG99	27AUG99
P2N2125A	10	8.00	80.00	03SEP99	16SEP99
P2N3100	6	8.00	48.00	03SEP99	10SEP99
P2N3110	9	16.00	144.00	13SEP99	23SEP99
P2N3225A	5	8.00	40.00	13SEP99	17SEP99
P1N2240	9	16.00	144.00	27OCT99	08NOV99
P1N2250	7	8.00	56.00	09NOV99	17NOV99
P2N2198	4	8.00	32.00	31JAN00	03FEB00
Highway Laborer					
P1N1202	20	0.00	320.00	17DEC98	15JAN99
P2N2115B	4	16.00	64.00	30AUG99	02SEP99
P2N2196	9	32.00	288.00	18JAN00	28JAN00
Skilled Laborer					
P1N1210	10	0.00	160.00	18MAR99	30MAR99
Loader/Backhoe 80 H.P.					
P1N1150	5	0.00	5.00	30NOV98	07DEC98
P1N2115A	8	0.00	0.00	23JUN99	02JUL99
P1N2210	12	1.00	12.00	12AUG99	27AUG99
P2N2115B	4	1.00	4.00	30AUG99	02SEP99
P2N2125A	10	1.00	10.00	03SEP99	16SEP99
P2N3110	9	1.00	9.00	13SEP99	23SEP99
Plastic Netting					
P1N2105B	15	2,500.00	37,500.00	06JUL99	26JUL99

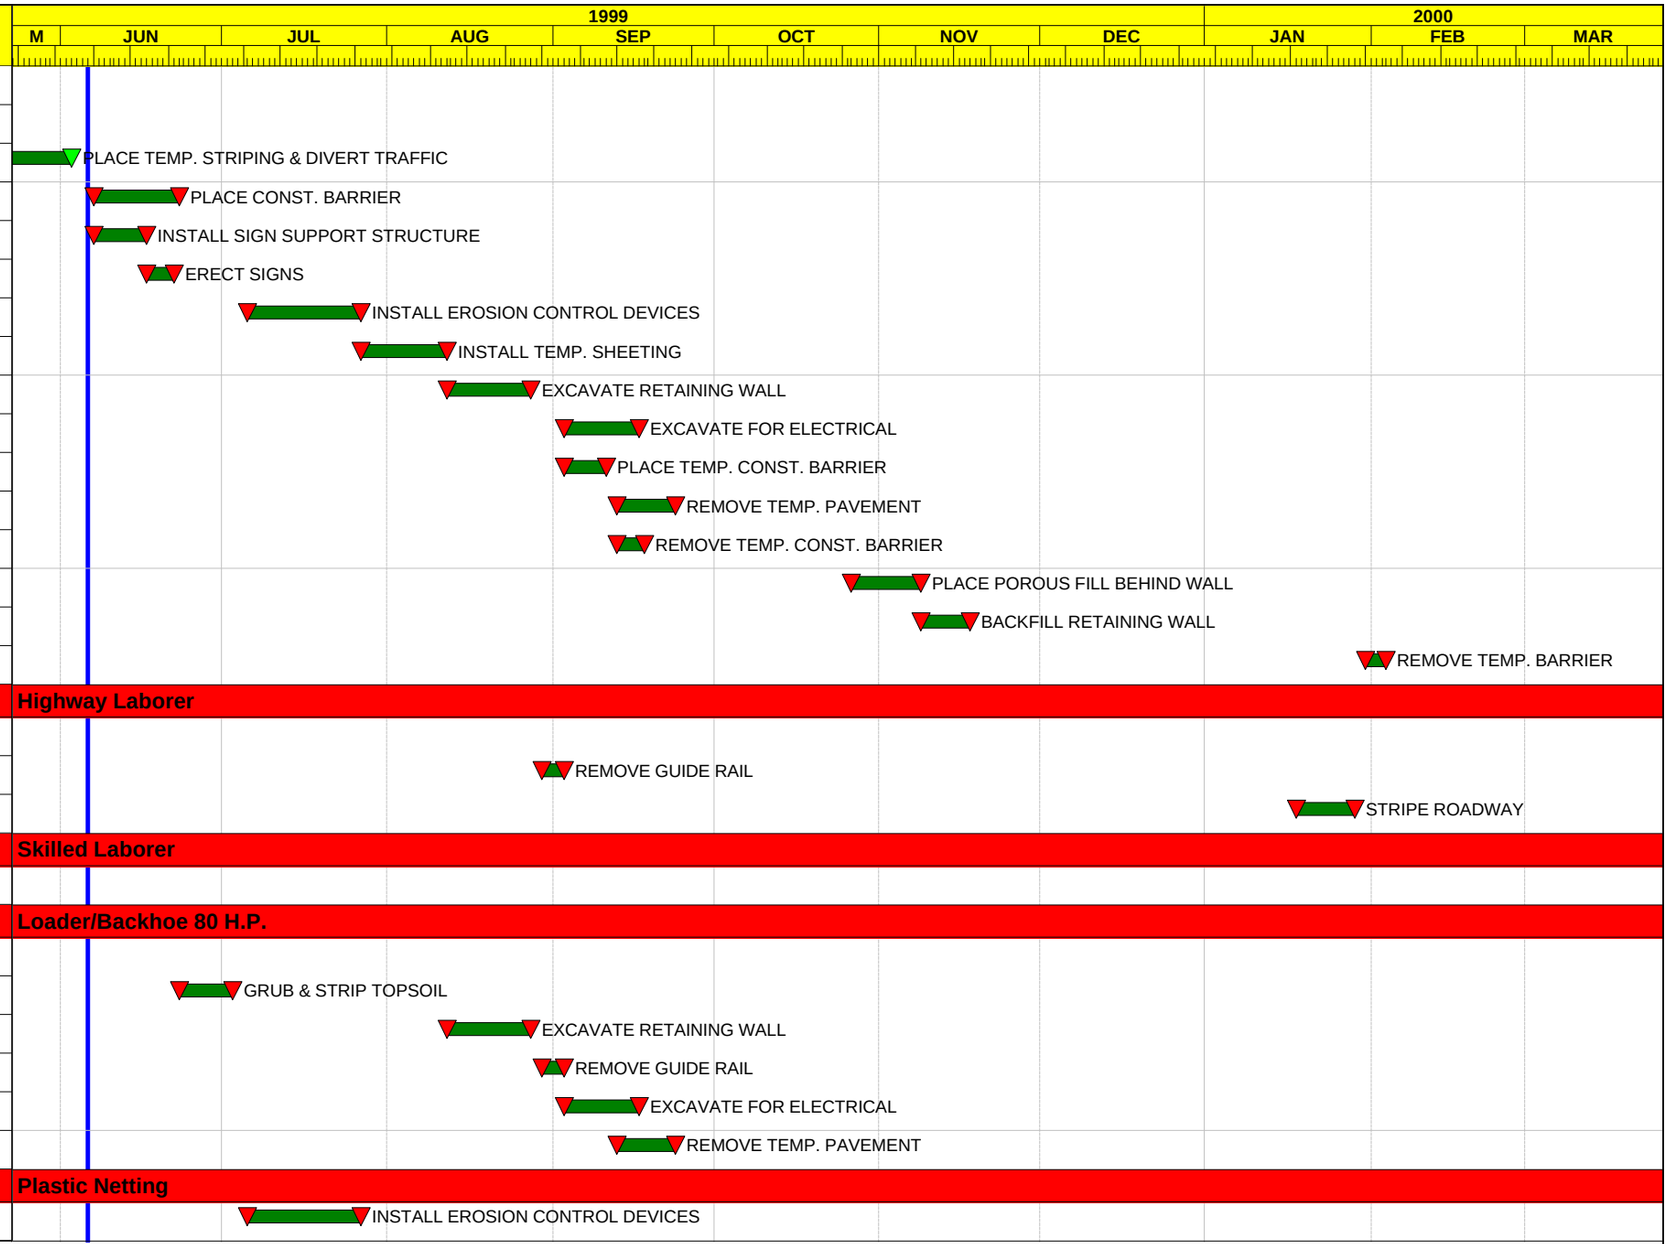

Project Start 24SEP98
Project Finish 28MAR00
Data Date 06JUN99
Run Date 25MAR99

Resource Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

HWY1

C.M. Construction, Inc.

Highway Widening

Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
Equipment Operator					
P1N1145	1	0.00	8.00	04NOV98	25NOV98
P1N1202	20	0.00	20.00	17DEC98	15JAN99
P1N1180	1	0.00	8.00	23DEC98	11JAN99
P1N1200	4	0.00	32.00	17FEB99	17MAR99
P1N1235	1	0.00	8.00	13MAY99	13MAY99
P1N2100	12	0.00	0.00	07JUN99	22JUN99
P1N2195	3	8.00	24.00	17JUN99	21JUN99
P1N2210	12	8.00	96.00	12AUG99	27AUG99
P2N2115B	4	8.00	32.00	30AUG99	02SEP99
P2N3100	6	8.00	48.00	03SEP99	10SEP99
P2N3110	9	8.00	72.00	13SEP99	23SEP99
P2N3225A	5	8.00	40.00	13SEP99	17SEP99
P2N3120	7	8.00	56.00	24SEP99	04OCT99
P1N2240	9	8.00	72.00	27OCT99	08NOV99
P1N2250	7	8.00	56.00	09NOV99	17NOV99
P2N2196	9	8.00	72.00	18JAN00	28JAN00
P2N2198	4	8.00	32.00	31JAN00	03FEB00
Equipment Operator - Light					
P1N2190	8	8.00	64.00	07JUN99	16JUN99
P2N2125A	10	8.00	80.00	03SEP99	16SEP99
Post Driver					
P1N2190	8	1.00	8.00	07JUN99	16JUN99
Sheeting Driver					
P1N2200	12	1.00	12.00	27JUL99	11AUG99
Paint Stripper, S.P.					
P2N2196	9	1.00	9.00	18JAN00	28JAN00
Truck - Flatbed, 3 Ton					
P1N2190	8	1.00	8.00	07JUN99	16JUN99
P2N2196	9	1.00	9.00	18JAN00	28JAN00
Dump Truck					
P1N2115A	8	1.00	8.00	23JUN99	02JUL99

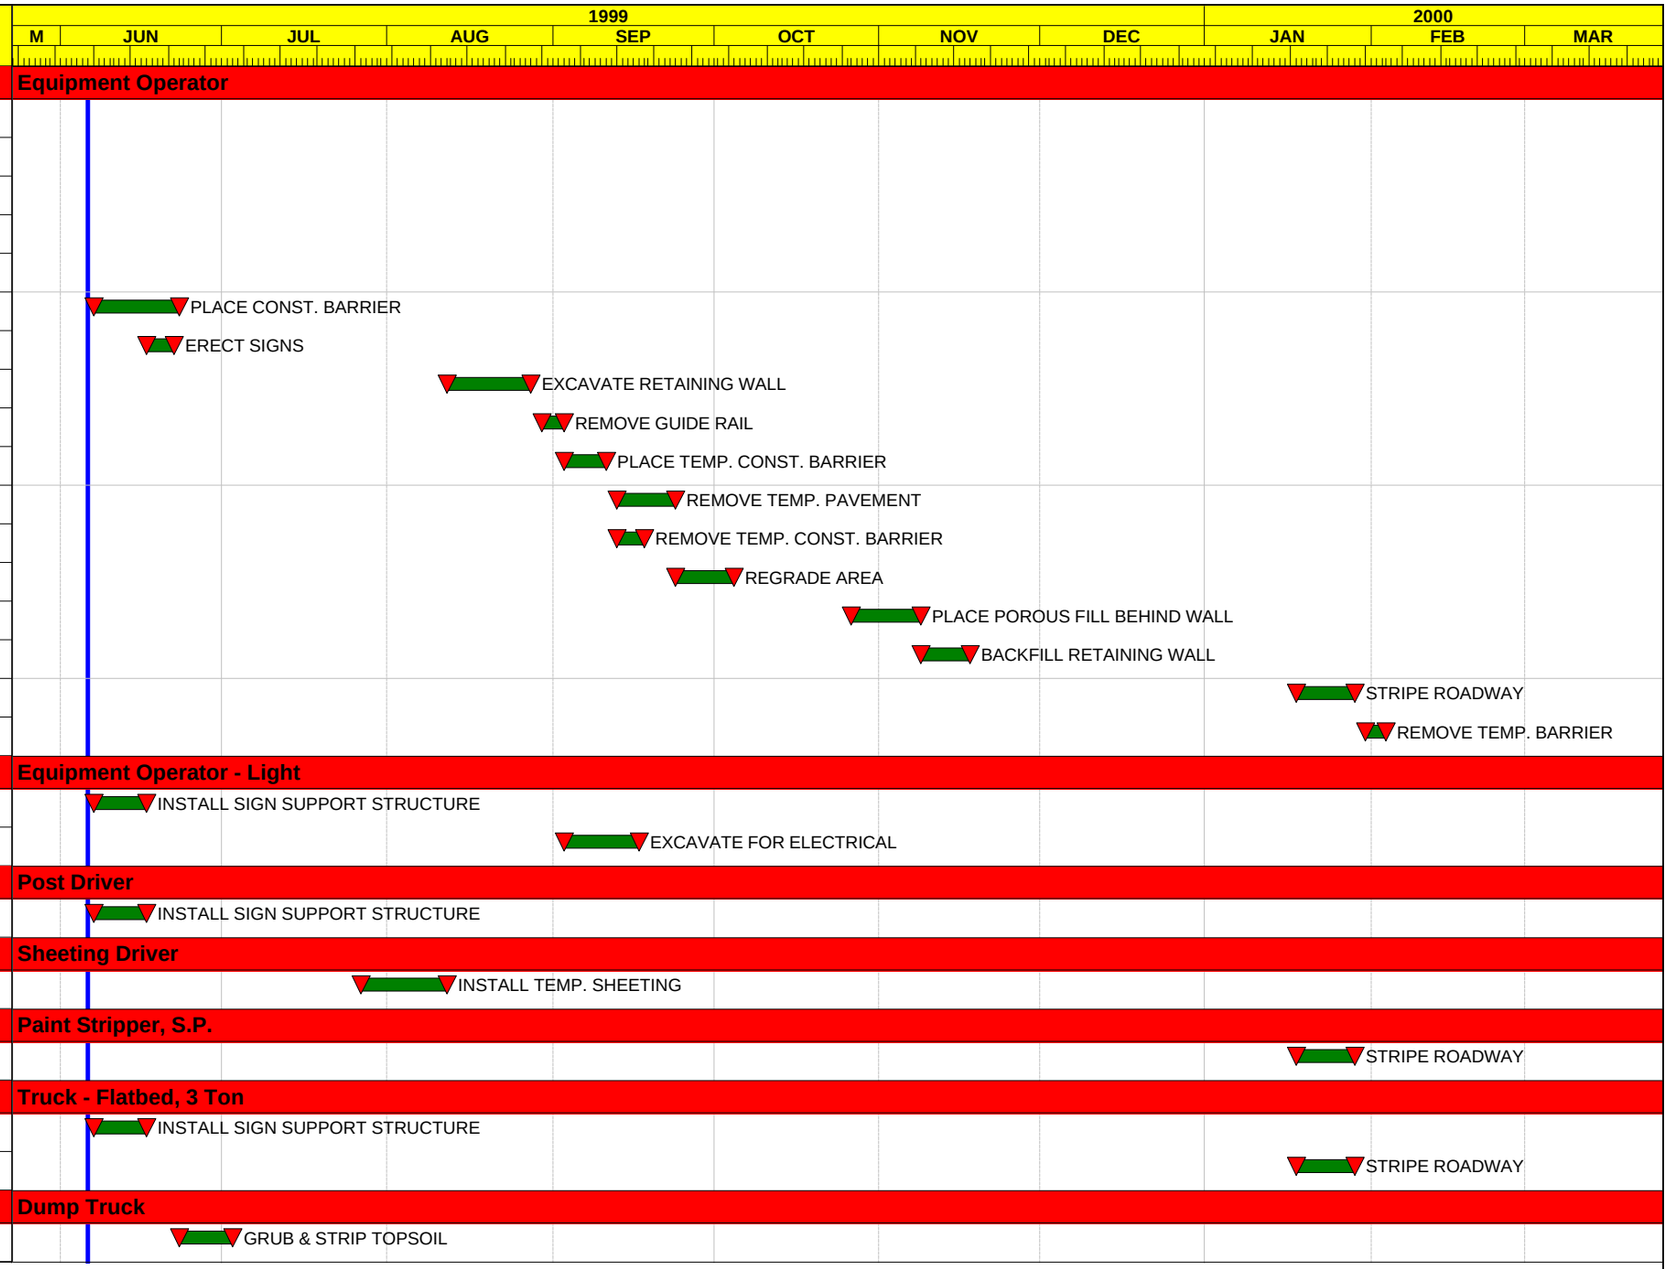

Project Start 24SEP98
Project Finish 28MAR00
Data Date 06JUN99
Run Date 25MAR99

Resource Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

HWY1

C.M. Construction, Inc.

Highway Widening

Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
Pete Reynolds - Electrical Crew Foreman					
Truck Crane					
P2N2130	19	1.00	19.00	24SEP99	20OCT99
Electrician					
P2N2125B	15	24.00	360.00	03SEP99	23SEP99
P2N2130	19	24.00	456.00	24SEP99	20OCT99
P2N2140	15	24.00	360.00	21OCT99	10NOV99
Foreman					
P2N2125B	15	2.00	30.00	03SEP99	23SEP99
P2N2130	19	2.00	38.00	24SEP99	20OCT99
P2N2140	15	2.00	30.00	21OCT99	10NOV99
Skilled Laborer					
P2N2130	19	16.00	304.00	24SEP99	20OCT99
P2N2140	15	16.00	240.00	21OCT99	10NOV99
Wiring					
P2N2140	15	10.00	150.00	21OCT99	10NOV99
Joe Martin - Structural Crew Foreman					
Concrete					
P1N2220	27	35.00	945.00	30AUG99	05OCT99
P1N2230	27	19.00	513.00	20SEP99	26OCT99
P1G5200	8	10.00	80.00	27OCT99	05NOV99
P1N2260	20	11.00	220.00	18NOV99	15DEC99
P1N2270	24	11.00	44.00	09DEC99	14DEC99
P1N2300	25	11.00	275.00	03JAN00	04FEB00
P1N2320	24	11.00	44.00	24JAN00	27JAN00
P1N3200	20	11.00	220.00	14FEB00	10MAR00
P1N3220	6	11.00	66.00	13MAR00	20MAR00
P1N3225B	6	11.00	66.00	21MAR00	28MAR00
Cement Finisher					
P1N2220	27	24.00	648.00	30AUG99	05OCT99
P1N2230	27	24.00	648.00	20SEP99	26OCT99
P1G5200	8	24.00	192.00	27OCT99	05NOV99

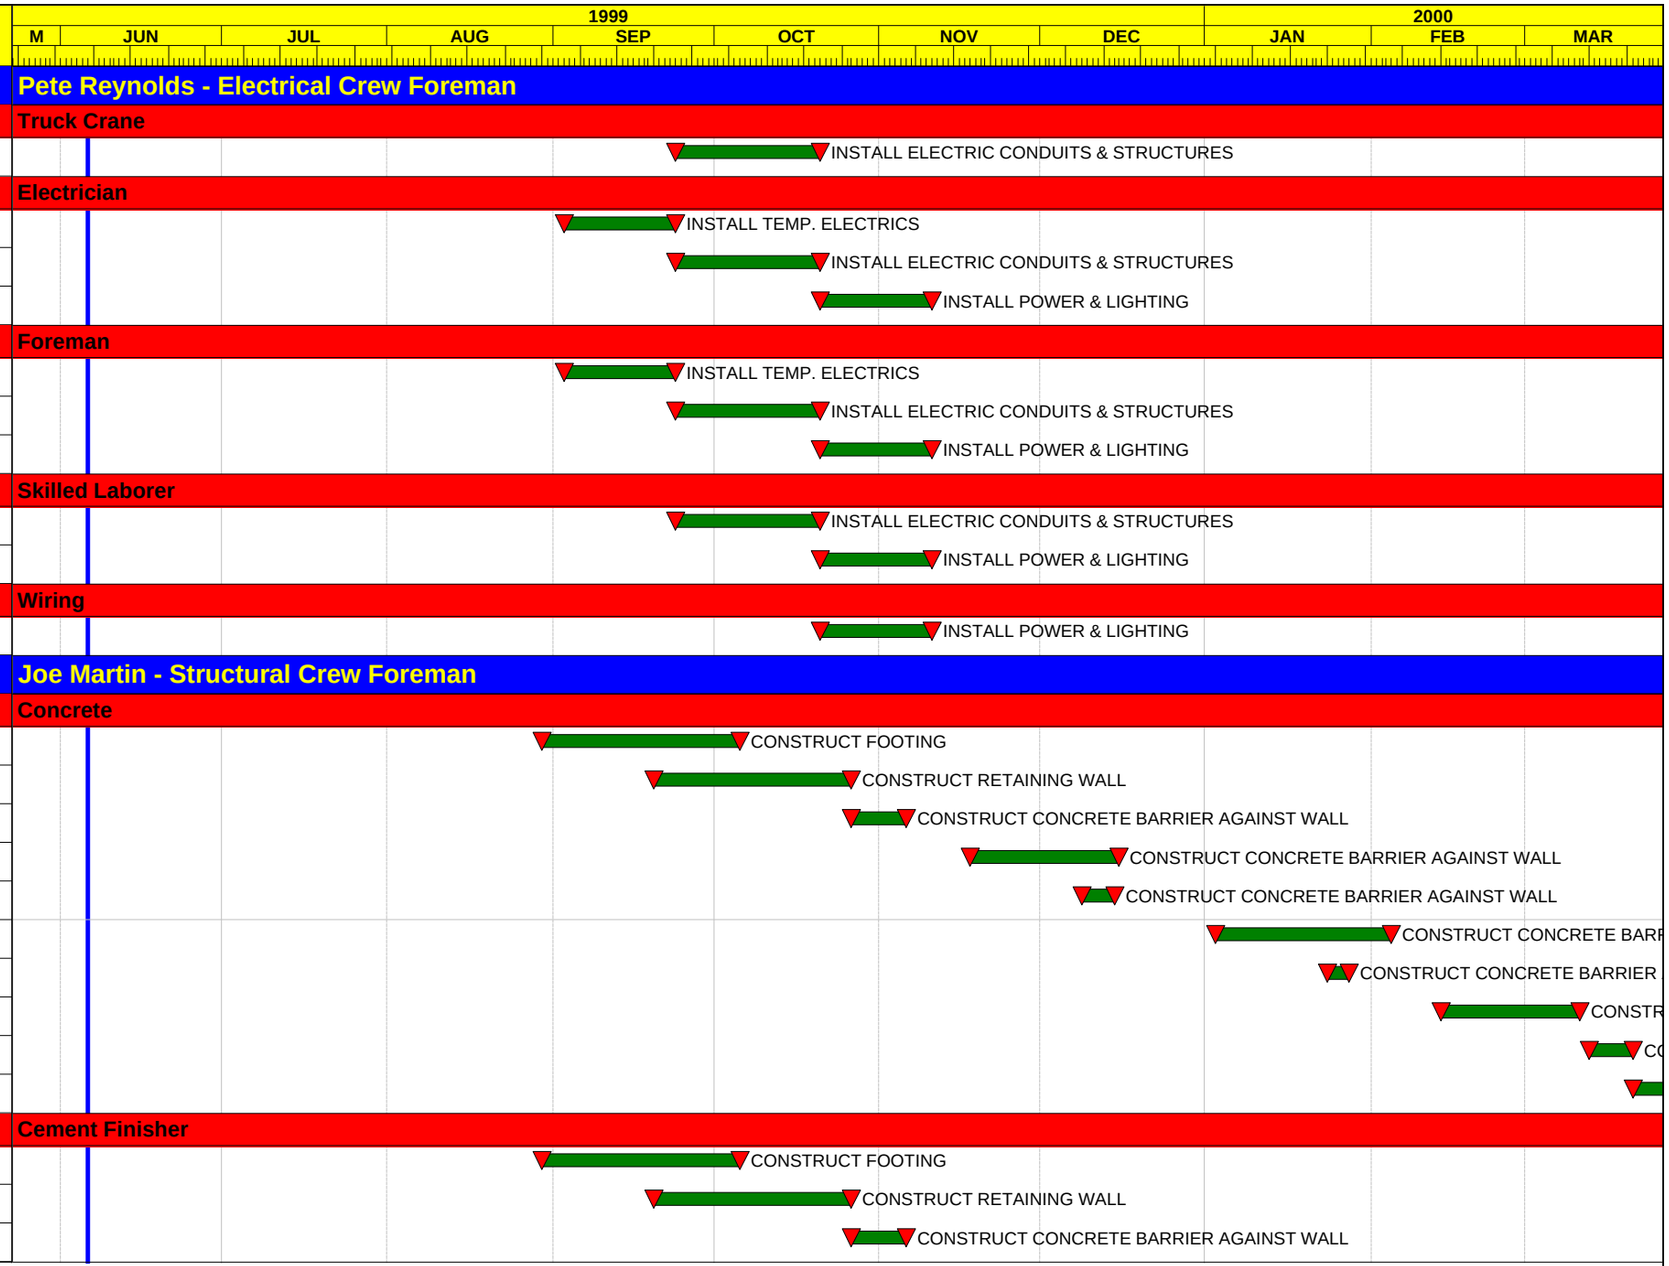

Project Start 24SEP98
Project Finish 28MAR00
Data Date 06JUN99
Run Date 25MAR99

Resource Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

HWY1

C.M. Construction, Inc.
Highway Widening
Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
P1N2260	20	24.00	480.00	18NOV99	15DEC99
P1N2270	24	4.00	96.00	09DEC99	13JAN00
P1N2300	25	24.00	600.00	03JAN00	04FEB00
P1N2320	24	4.00	96.00	24JAN00	24FEB00
P1N3200	20	24.00	480.00	14FEB00	10MAR00
P1N3220	6	24.00	144.00	13MAR00	20MAR00
P1N3225B	6	24.00	144.00	21MAR00	28MAR00
Foreman					
P1N2220	27	2.00	42.00	30AUG99	27SEP99
P1N2230	27	2.00	54.00	20SEP99	26OCT99
P1G5200	8	2.00	16.00	27OCT99	05NOV99
P1N2260	20	2.00	40.00	18NOV99	15DEC99
P1N2270	24	0.33	8.00	09DEC99	13JAN00
P1N2300	25	2.00	50.00	03JAN00	04FEB00
P1N2320	24	2.00	48.00	24JAN00	24FEB00
P1N3200	20	2.00	40.00	14FEB00	10MAR00
P1N3220	6	2.00	12.00	13MAR00	20MAR00
P1N3225B	6	2.00	12.00	21MAR00	28MAR00
General Laborer					
P1N2220	27	24.00	648.00	30AUG99	05OCT99
P1N2230	27	16.00	432.00	20SEP99	26OCT99
P1G5200	8	24.00	192.00	27OCT99	05NOV99
P1N2260	20	24.00	480.00	18NOV99	15DEC99
P1N2270	24	24.00	576.00	09DEC99	13JAN00
P1N2300	25	24.00	600.00	03JAN00	04FEB00
P1N2320	24	24.00	576.00	24JAN00	24FEB00
P1N3200	20	24.00	480.00	14FEB00	10MAR00
P1N3220	6	24.00	144.00	13MAR00	20MAR00
P1N3225B	6	24.00	144.00	21MAR00	28MAR00
Gas Engine Vibrator					
P1N2220	27	2.00	54.00	30AUG99	05OCT99

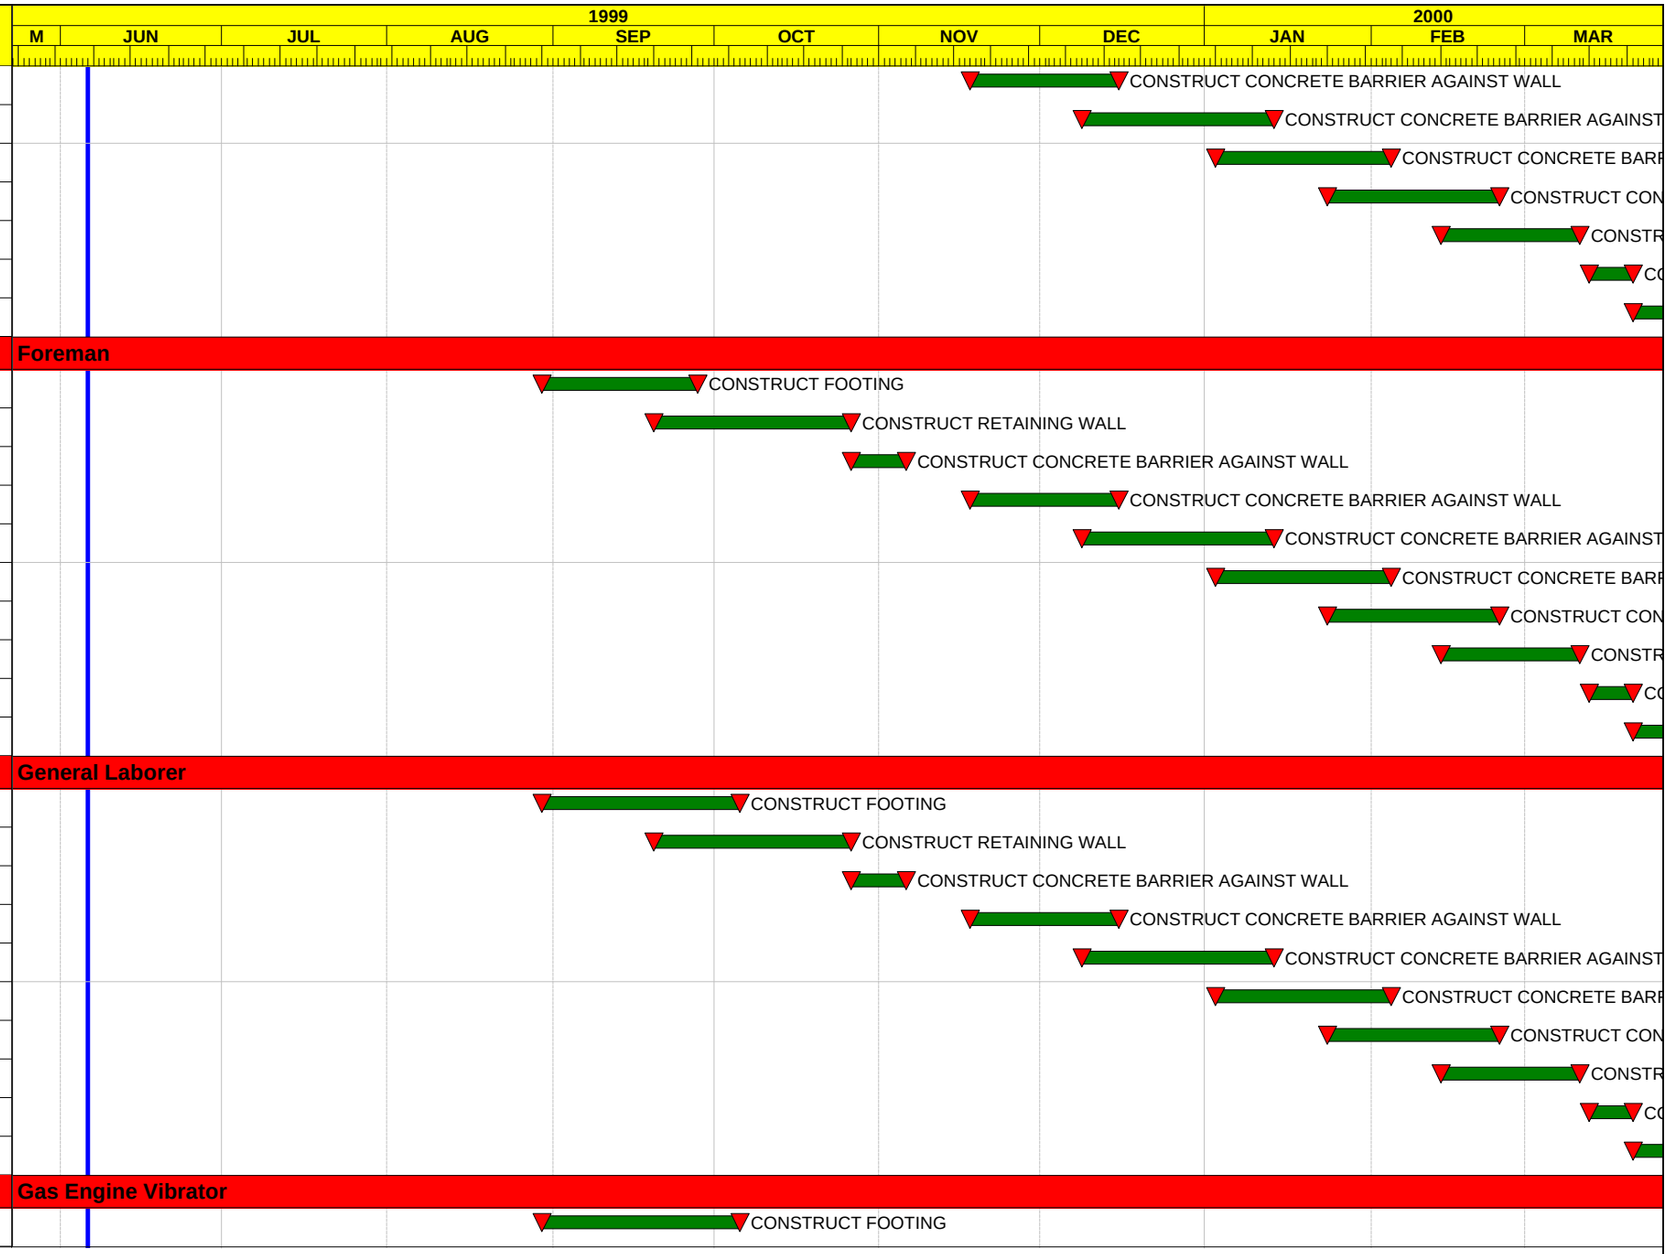

Project Start 24SEP98
Project Finish 28MAR00
Data Date 06JUN99
Run Date 25MAR99

© Primavera Systems, Inc.

Resource Bar
Progress Bar
Critical Activity

HWY1

C.M. Construction, Inc.

Highway Widening

Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
P1N2230	27	2.00	54.00	20SEP99	26OCT99
P1G5200	8	2.00	16.00	27OCT99	05NOV99
P1N2260	20	2.00	40.00	18NOV99	15DEC99
P1N2270	24	2.00	48.00	09DEC99	13JAN00
P1N2300	25	2.00	50.00	03JAN00	04FEB00
P1N2320	24	2.00	48.00	24JAN00	24FEB00
P1N3200	20	2.00	40.00	14FEB00	10MAR00
P1N3220	6	2.00	12.00	13MAR00	20MAR00
P1N3225B	6	2.00	12.00	21MAR00	28MAR00
Joyce A. Miller - Paving Crew Foreman					
Asphalt Surface Course					
P1N1185	3	0.00	22,500.00	07JAN99	19JAN99
P1N1230	3	0.00	22,500.00	03MAY99	07MAY99
P2N2185	10	7,725.00	77,250.00	04JAN00	17JAN00
Asphalt Base Course					
P1N1170	6	0.00	46,350.00	14DEC98	22DEC98
P1N1220	4	0.00	30,900.00	15APR99	29APR99
P2N2170	10	7,725.00	77,250.00	01DEC99	14DEC99
Dozer, 200 H.P.					
P1N1170	6	0.00	4.00	14DEC98	22DEC98
P1N1220	4	0.00	4.00	15APR99	29APR99
P2N2170	10	1.00	10.00	01DEC99	14DEC99
Foreman					
P1N1170	6	0.00	12.00	14DEC98	22DEC98
P1N1185	3	0.00	6.00	07JAN99	19JAN99
P1N1220	4	0.00	8.00	15APR99	29APR99
P1N1230	3	0.00	6.00	03MAY99	07MAY99
P2N2150	14	2.00	28.00	11NOV99	30NOV99
P2N2170	10	2.00	20.00	01DEC99	14DEC99
P2N2180	12	2.00	24.00	15DEC99	03JAN00
P2N2185	10	2.00	20.00	04JAN00	17JAN00

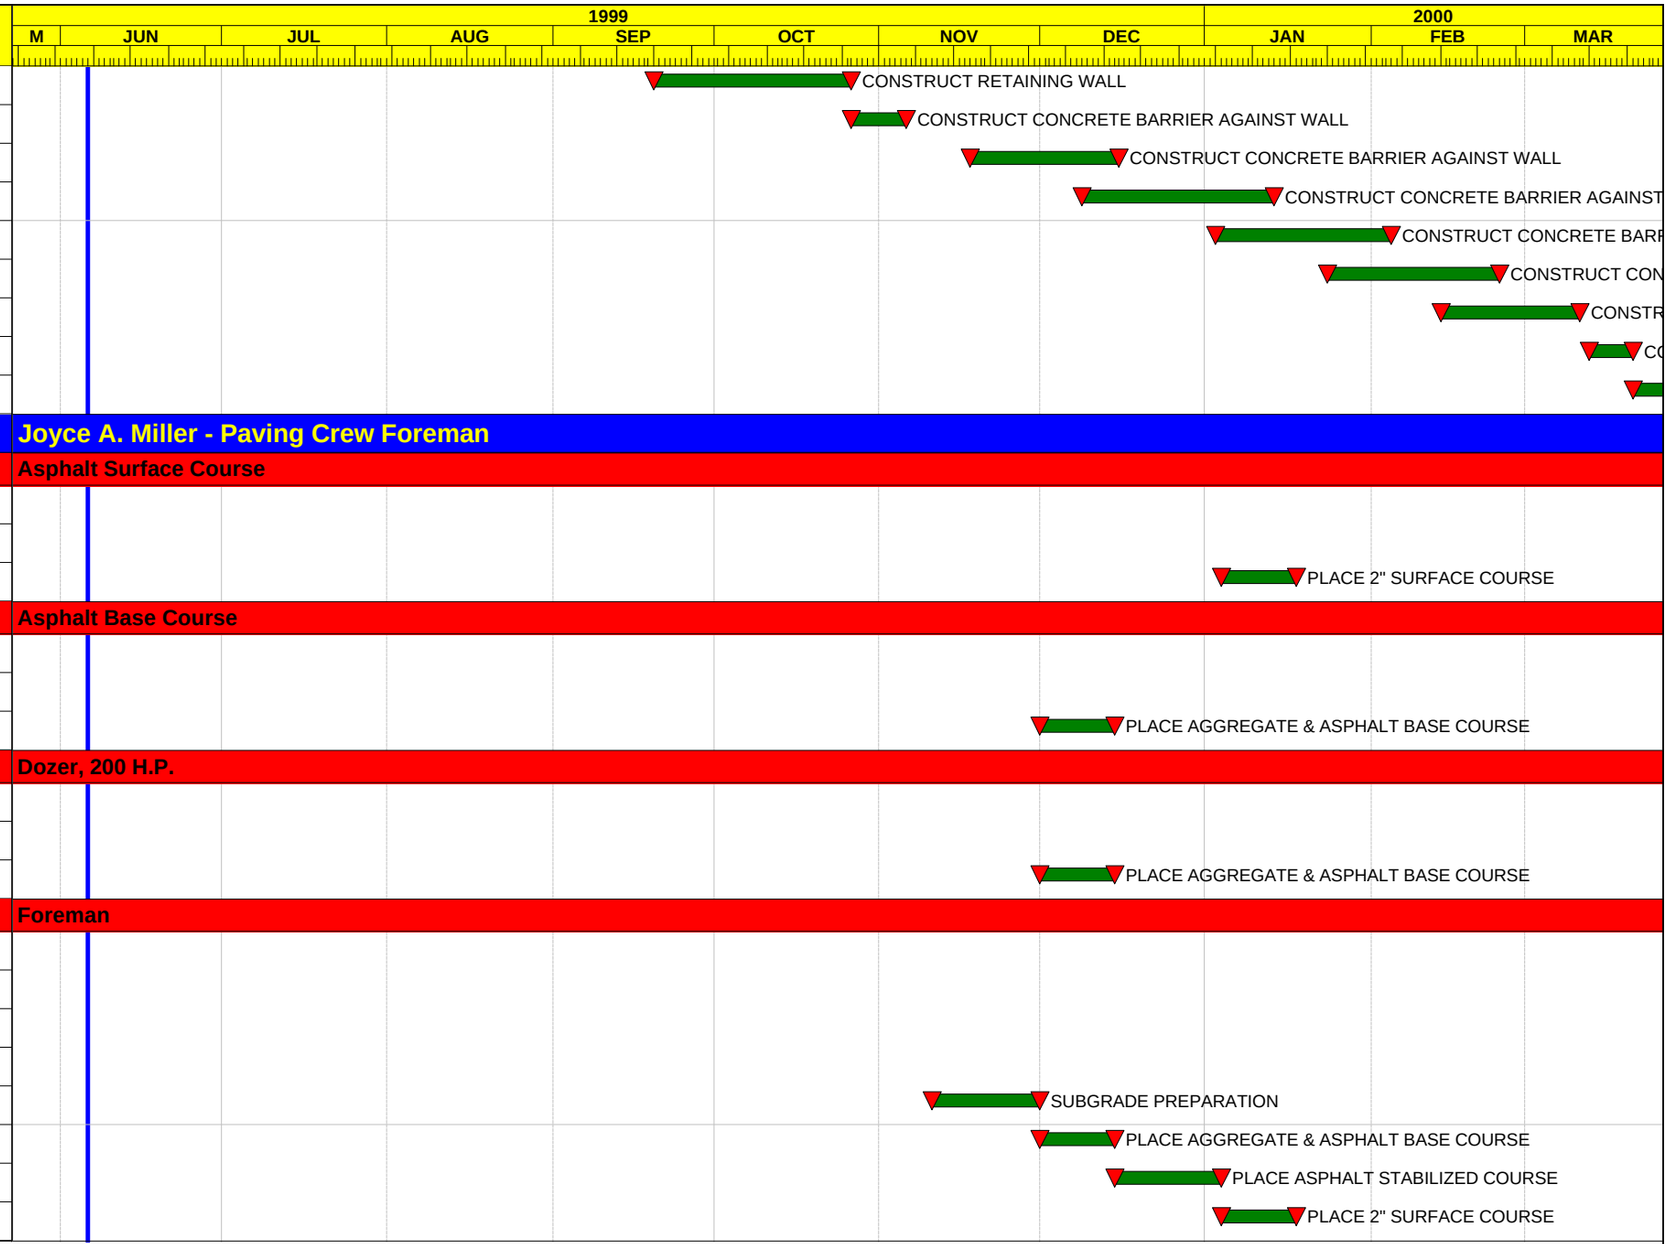

Project Start 24SEP98
Project Finish 28MAR00
Data Date 06JUN99
Run Date 25MAR99

Resource Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

HWY1

C.M. Construction, Inc.
Highway Widening
Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
General Laborer					
P1N1220	4	0.00	64.00	15APR99	29APR99
Highway Laborer					
P1N1170	6	0.00	48.00	14DEC98	22DEC98
P1N1185	3	0.00	72.00	07JAN99	19JAN99
P1N1230	3	0.00	96.00	03MAY99	07MAY99
P2N2150	14	8.00	112.00	11NOV99	30NOV99
P2N2170	10	16.00	160.00	01DEC99	14DEC99
P2N2180	12	18.00	216.00	15DEC99	03JAN00
P2N2185	10	8.00	80.00	04JAN00	17JAN00
Equipment Operator					
P1N1185	3	0.00	72.00	07JAN99	19JAN99
P1N1220	4	0.00	96.00	15APR99	29APR99
P1N1230	3	0.00	48.00	03MAY99	07MAY99
P2N2150	14	8.00	112.00	11NOV99	30NOV99
P2N2170	10	24.00	240.00	01DEC99	14DEC99
P2N2180	12	8.00	96.00	15DEC99	03JAN00
P2N2185	10	8.00	80.00	04JAN00	17JAN00
Asphalt Paver, 130 H.P.					
P1N1185	3	0.00	3.00	07JAN99	19JAN99
P1N1230	3	0.00	3.00	03MAY99	07MAY99
P2N2180	12	1.00	12.00	15DEC99	03JAN00
P2N2185	10	1.00	10.00	04JAN00	17JAN00
Roller, Tandem					
P1N1170	6	0.00	4.00	14DEC98	22DEC98
P1N1220	4	0.00	4.00	15APR99	29APR99
P2N2170	10	1.00	10.00	01DEC99	14DEC99
Roller, Steel Wheel					
P1N1185	3	0.00	3.00	07JAN99	19JAN99
P1N1230	3	0.00	6.00	03MAY99	07MAY99
P2N2150	14	1.00	14.00	11NOV99	30NOV99
P2N2180	12	1.00	12.00	15DEC99	03JAN00

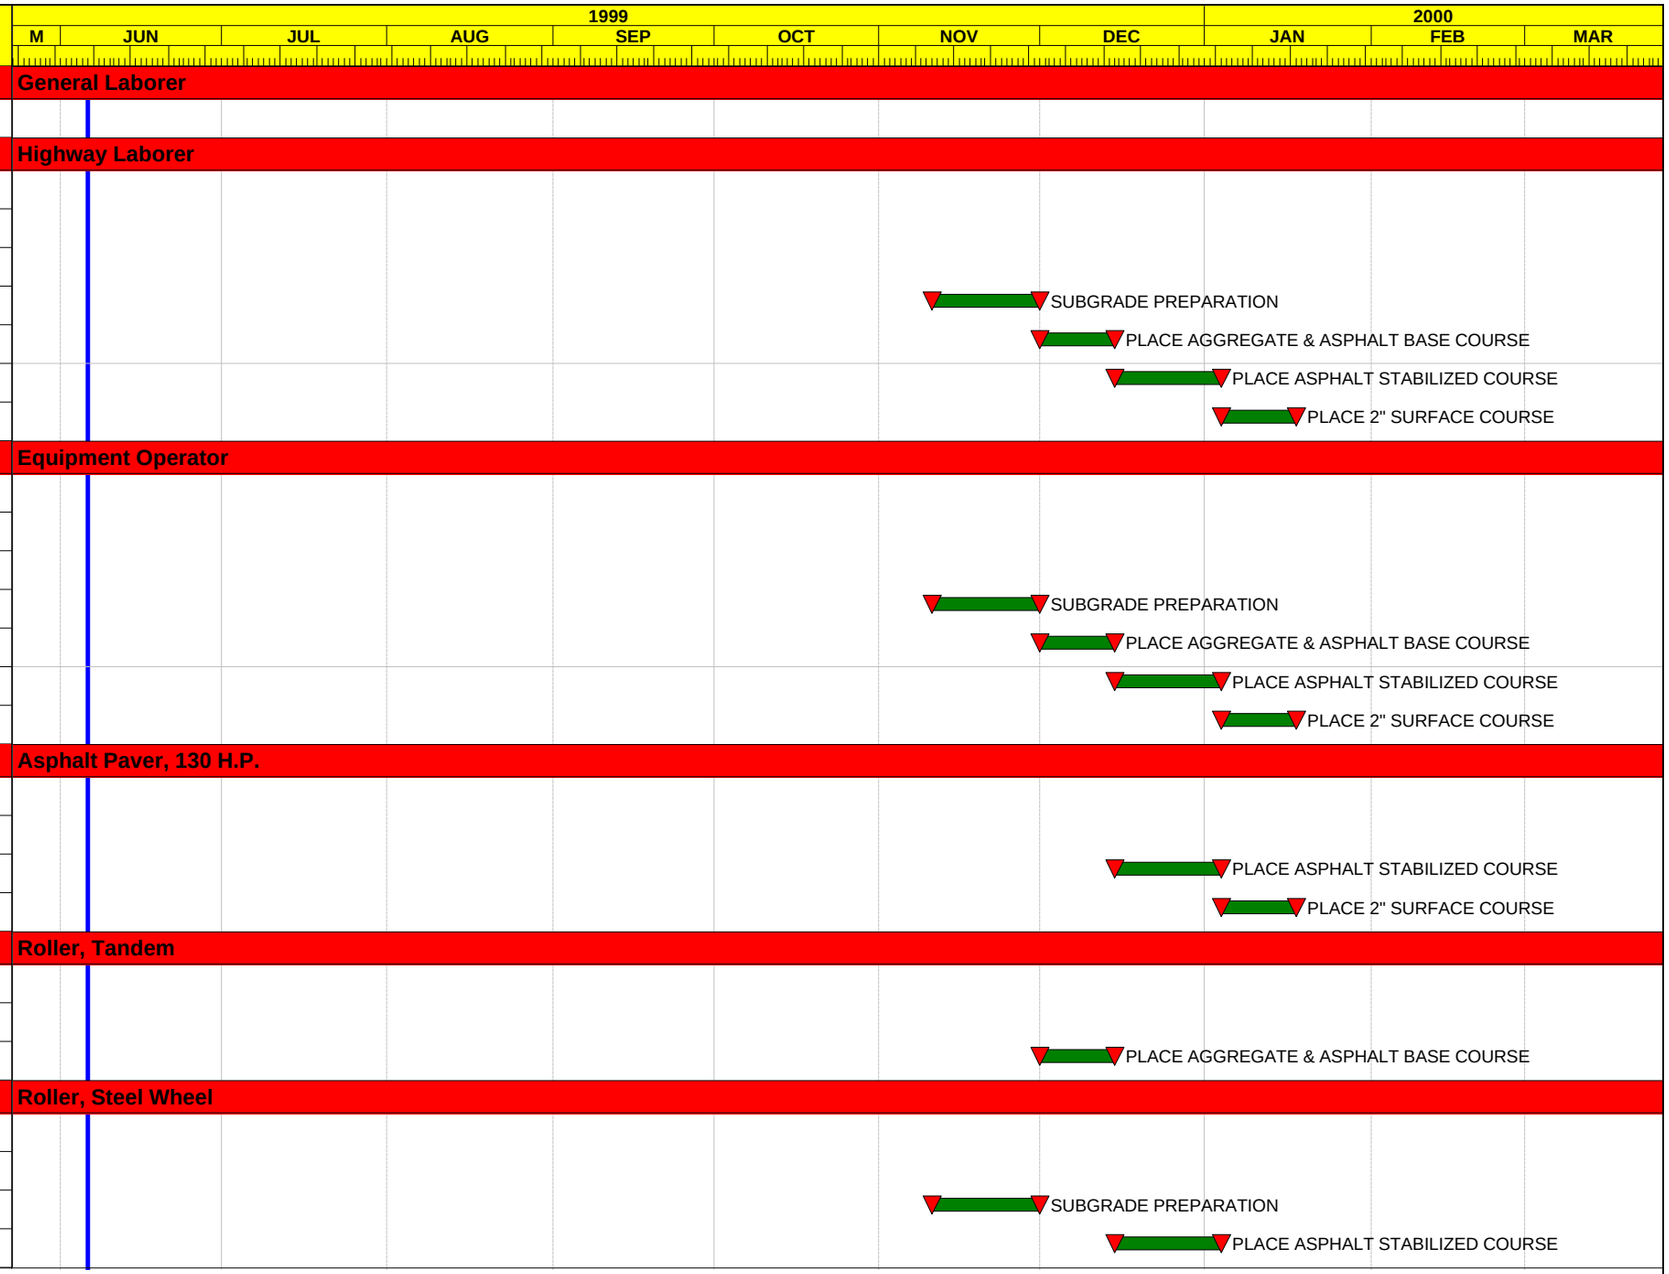

Project Start	24SEP98
Project Finish	28MAR00
Data Date	06JUN99
Run Date	25MAR99

Resource Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

HWY1

C.M. Construction, Inc.

Highway Widening

Resource Analysis

Activity ID	Orig Dur	Units Per Day	Budgeted Quantity	Resource early start	Resource early finish
P2N2185	10	1.00	10.00	04JAN00	17JAN00
Aggregate Spreader					
P1N1170	6	0.00	4.00	14DEC98	22DEC98
P1N1220	4	0.00	4.00	15APR99	29APR99
P2N2170	10	1.00	10.00	01DEC99	14DEC99
Asphalt Stabilized Course					
P2N2180	12	6,437.50	77,250.00	15DEC99	03JAN00

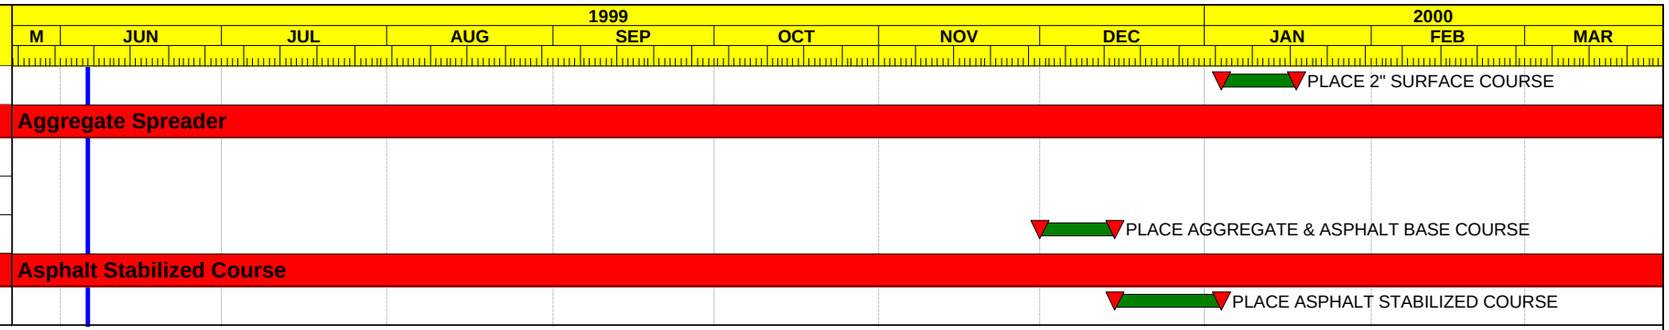

Project Start 24SEP98
Project Finish 28MAR00
Data Date 06JUN99
Run Date 25MAR99

© Primavera Systems, Inc.

Resource Bar
Progress Bar
Critical Activity

HWY1

C.M. Construction, Inc.
Highway Widening
Resource Analysis
